



*Town of Chatham*  
*Office of the Select Board*  
*Town Manager*  
*549 Main Street*  
*Chatham, MA 02633*



Jill R. Goldsmith  
TOWN MANAGER  
[jgoldsmith@chatham-ma.gov](mailto:jgoldsmith@chatham-ma.gov)

Tel: (508) 945-5105  
Fax: (508) 945-3550  
[www.chatham-ma.gov](http://www.chatham-ma.gov)

**NEWS RELEASE**

FOR IMMEDIATE RELEASE – September 3, 2021

**Media Contact:**

Robert Duncanson, Ph.D., Director of Health & Natural Resources  
Town of Chatham  
(508) 945-5165  
[rduncanson@chatham-ma.gov](mailto:rduncanson@chatham-ma.gov)

---


**Sewer Construction Update**

Chatham – Robert B. Our Co., Inc. will be continuing work for the Stony Hill/Crowell Road Infrastructure Project. Work this summer will include stormwater infrastructure installation and limited water main work. Robert B. Our Co., Inc. plans to start this project with one crew, weather permitting.


**Work for the week of September 6<sup>th</sup> – September 10<sup>th</sup>: **\*\*No Work on Labor Day (9/6)\*\*****  
**\*DETOUR\***

- Commence sidewalk restorations along Crowell Road.
- Continue pavement preparation along Stony Hill Road, Lake Street, and Crowell Road.
- Continue stormwater work on Stony Hill Road.

**\*\*Detour\*\*** - Portion of Crowell Road will be closed between Stony Hill Road and Tip Cart Drive, and Lake Street will also be closed. Traffic will be detoured via Tip Cart to Barcliff Ave to Old Harbor Road to Orleans Road to Stony Hill Road.

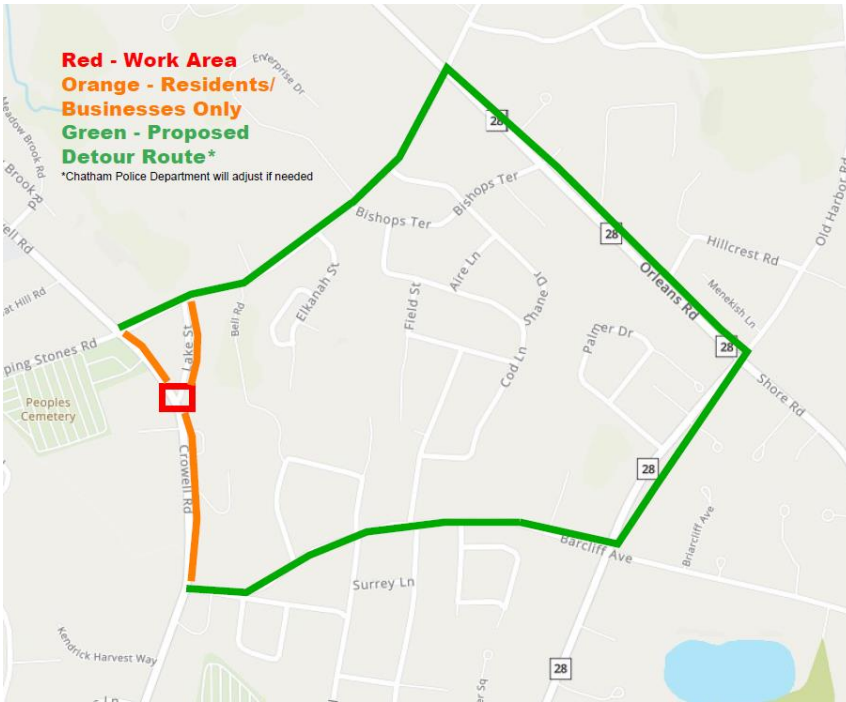

**\*\*Detour\*\*** - Portion of Stony Hill Road will be closed between Crowell Road and Lake Street. Traffic will be detoured through Lake Street.

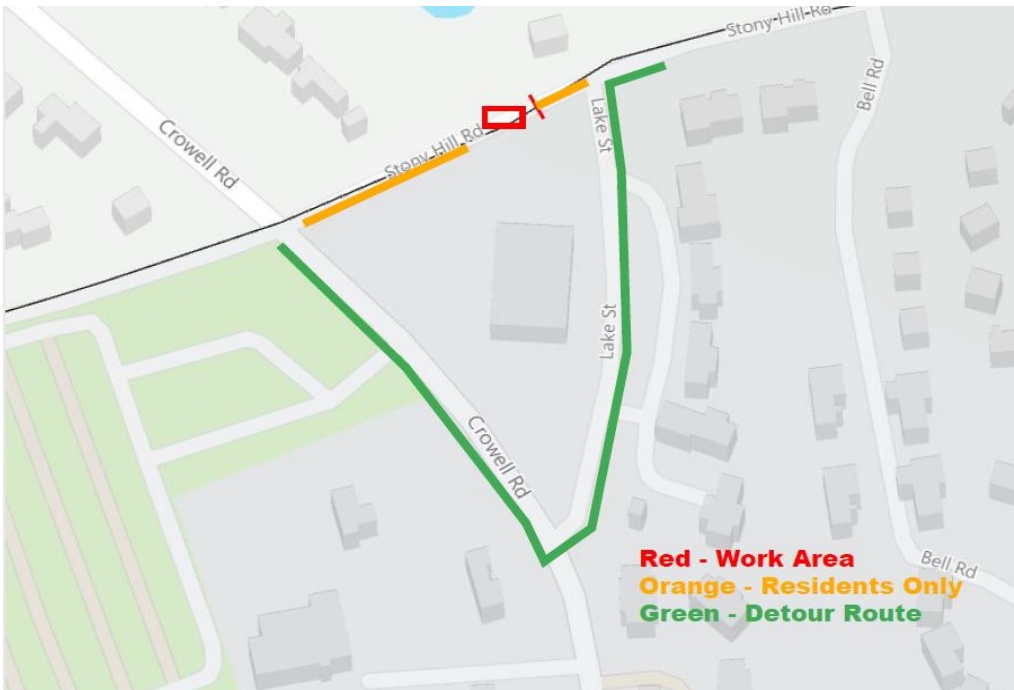

Note: Detours may vary day to day as the road work will move quickly between the construction areas.

**One Week Look Ahead (9/13– 9/17):**

**\*NEW DETOUR\***

- Commence final grading and paving along Stony Hill Road, Lake Street, and Crowell Road.
- \*Tentative\* Final pavement of Harding’s Lane.

**\*\*Detour\*\* - TBD.**

**Two Week Look Ahead (9/20– 9/24):**

**\*NEW DETOUR\***

- Continue final grading and paving along Stony Hill Road, Lake Street, and Crowell Road.

**\*\*Detour\*\* - TBD.**

Please note that this is a projected schedule and will be adjusted accordingly based on the Contractor’s actual progress and the weather. On an as needed basis auxiliary crews will be performing testing, installing inverts, raising castings, paving, and performing general cleanup at various locations throughout the project area.

Roads will be passable at the end of each day. Police Details and Contractors will work with residents to ensure their needs for access are addressed.

Police Details and signage will be in-place to assist motorists in reaching their destination.

Normal work hours are 7:00 AM to 4:00 PM Monday to Friday, weather permitting, unless otherwise noted.

We encourage you to visit the sewer construction project web site for updated schedule information and weekly press releases at: <http://www.chathamscproject.info> and the Town’s website for additional information regarding the CWMP and other important projects and events in the Town at: <http://www.chatham-ma.gov>.

Thank you for your patience and cooperation during this important project to restore and protect our environment.

###
